


Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	%	2012												2013					2014							
							JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	
Startup																															
		40d	0	18JUL12 A	12SEP12 A	100	[Progress bar]																								
0001	NTP	0	0	18JUL12 A		100	◆ NTP																								
0010	Kickoff Meeting at BTM	0	0	23JUL12 A		100	◆ Kickoff Meeting at BTM																								
0011	Kickoff w/Bryant Assoc.	0	0	26JUL12 A		100	◆ Kickoff w/Bryant Assoc.																								
0012	Team Kickoff Meeting	0	0	02AUG12 A		100	◆ Team Kickoff Meeting																								
0013	Kickoff with Kelley Chunn	0	0	08AUG12 A		100	◆ Kickoff with Kelley Chunn																								
0014	Kickoff with Bioengineering Group	0	0	12SEP12 A		100	◆ Kickoff with Bioengineering Group																								
Task 1: Existing Conditions																															
		320d	0	31OCT11 A	23JAN13 A	100	[Progress bar]																								
Topo Survey																															
		133d	0	19JUL12 A	23JAN13 A	100	[Progress bar]																								
1001	Survey NTP	0	0	19JUL12 A		100	◆ Survey NTP																								
1002	Survey Kickoff Meeting	0	0	26JUL12 A		100	◆ Survey Kickoff Meeting																								
1010	Field Survey	40d	0	26JUL12 A	05OCT12 A	100	▶ Field Survey																								
1011	Prepare Survey Base Plans	15d	0	08OCT12 A	22JAN13 A	100	▶ Prepare Survey Base Plans																								
1012	95% Base Plan Submission	0	0		14NOV12 A	100	▶ 95% Base Plan Submission																								
1013	Final Base Plan Submission	0	0		23JAN13 A	100	▶ Final Base Plan Submission																								
Data Gathering																															
		50d	0	31OCT11 A	31OCT12 A	100	[Progress bar]																								
1101	Gathering Reports + Data	50d	0	31OCT11 A	31OCT12 A	100	[Progress bar]																								
Conditions Survey																															
		53d	0	20AUG12 A	31OCT12 A	100	[Progress bar]																								
1210	Conditions Survey	20d	0	20AUG12 A	31OCT12 A	100	[Progress bar]																								
1220	Site walk w/BTD	0	0	20AUG12 A		100	◆ Site walk w/BTD																								
Task 2: Concept Design																															
		164d	43d	09SEP12 A	29APR13	92	[Progress bar]																								
Coordination & Review w/BTD																															
		124d	3d	09SEP12 A	08MAR13	100	[Progress bar]																								
2210	Discuss Initial Concepts	30d	0	09SEP12 A	28FEB13 A	100	▶ Discuss Initial Concepts																								
2220	Concept Mtg. w/BTD/Public Mtg. #1 Debrief	0	0	05NOV12 A		100	▶ Concept Mtg. w/BTD/Public Mtg. #1 Debrief																								
2221	Review of Circulation Concepts w/BTD, BRA	0	0		30NOV12 A	100	◆ Review of Circulation Concepts w/BTD, BRA																								
2222	Review of Circulation w/BTD + BRA	0	0	09JAN13 A		100	▶ Review of Circulation w/BTD + BRA																								
2223	Review of Circulation w/BTD +BRA	0	0	15JAN13 A		100	▶ Review of Circulation w/BTD +BRA																								
2224	Review w/BTD + BRA	0	0	05FEB13 A		100	◆ Review w/BTD + BRA																								

Start date 18JUL12
 Finish date 24NOV15
 Data date 28FEB13
 Run date 28FEB13
 Page number 1A
 © Primavera Systems, Inc.

Parsons Brinckerhoff Dudley Sq. Streetscape

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	%	2012					2013					2014						
							JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV

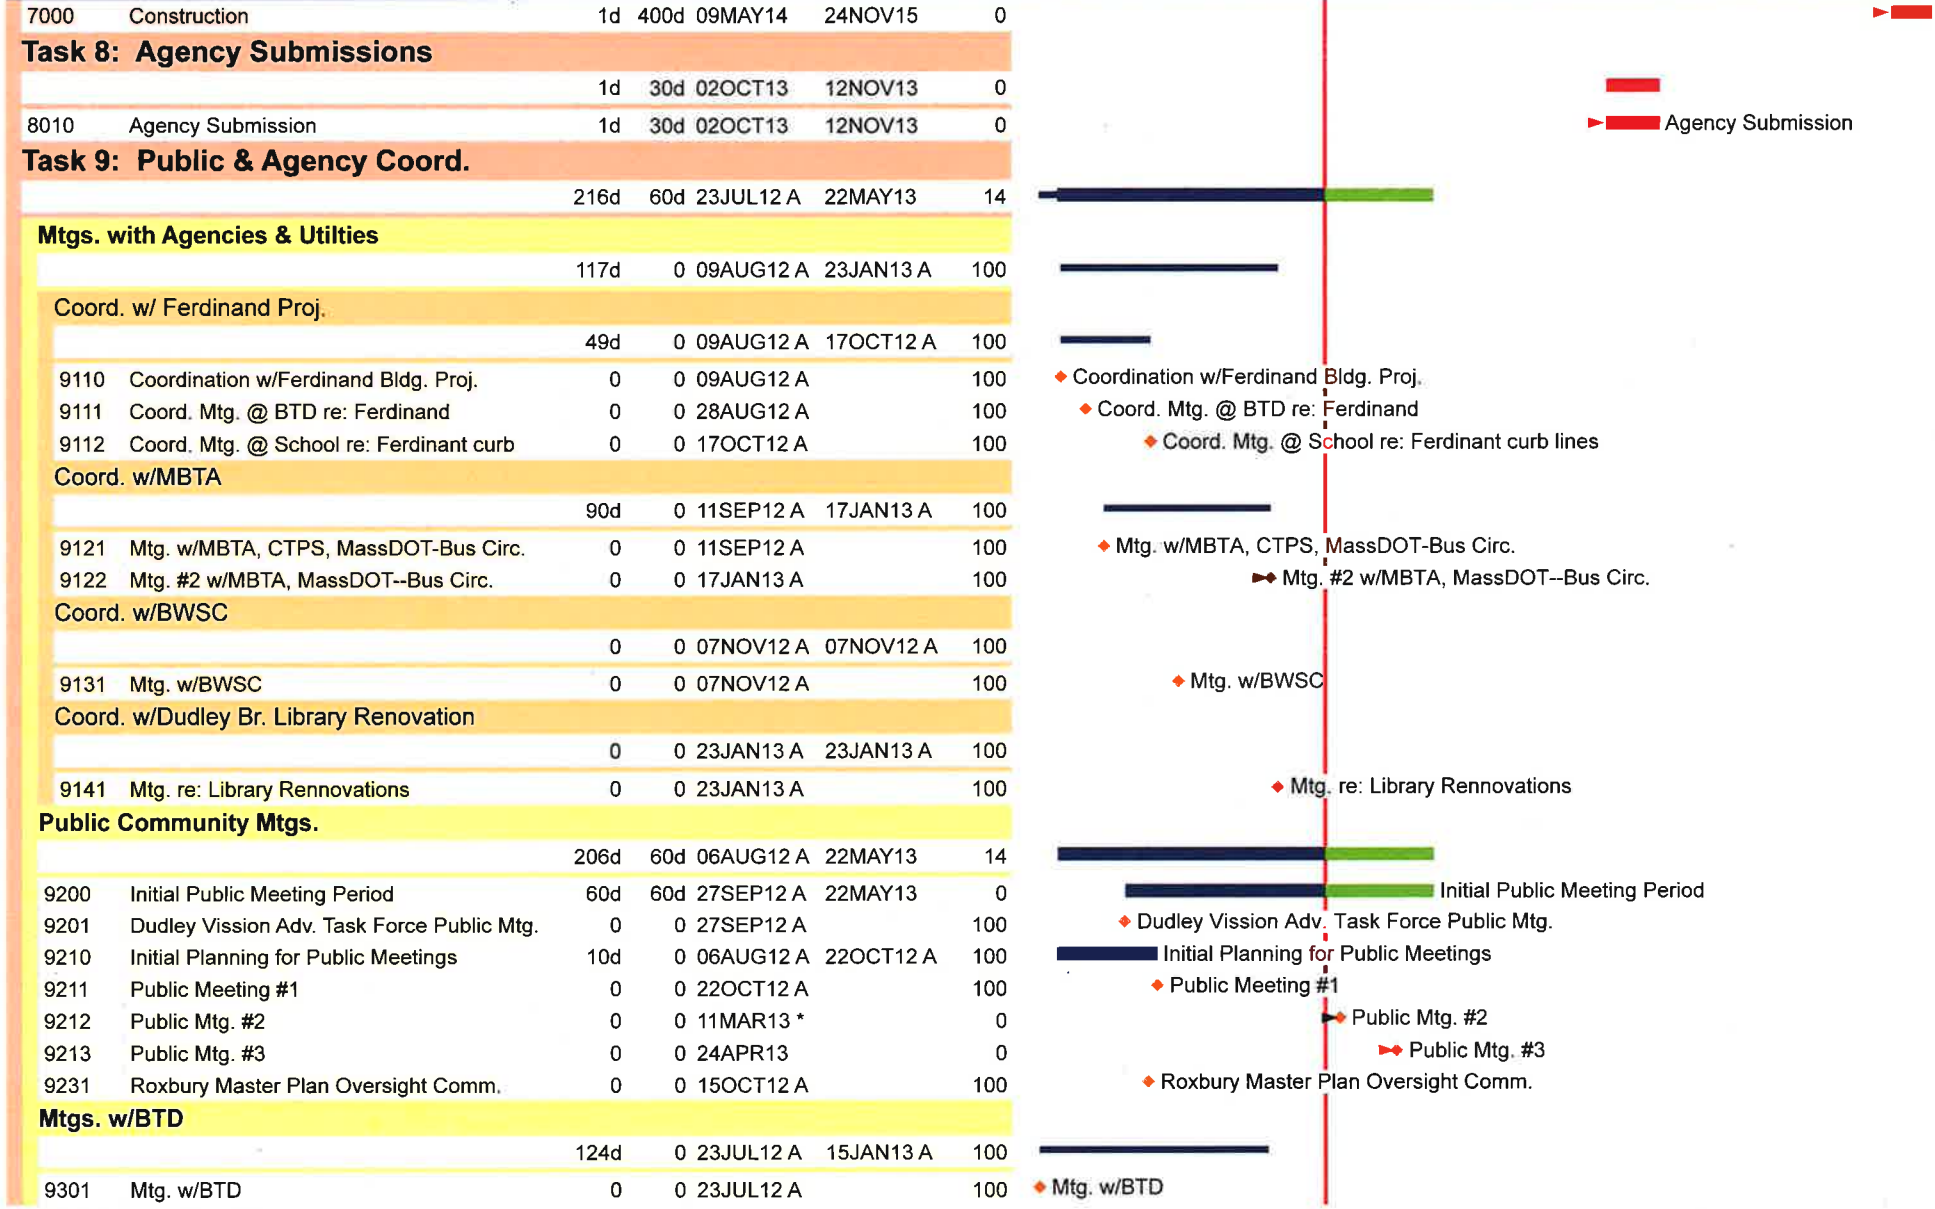

Start date 18JUL12
 Finish date 24NOV15
 Data date 28FEB13
 Run date 28FEB13
 Page number 3A
 © Primavera Systems, Inc.

**Parsons Brinckerhoff
 Dudley Sq. Streetscape**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	%	2012					2013					2014																						
							JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN									
9311	Mtg. w/BTD on circulation	0	0	09JAN13	A	100							◆																										
9312	Mtg. w/BTD on circulation	0	0	15JAN13	A	100							▶◆																										

Start date 18JUL12
 Finish date 24NOV15
 Data date 28FEB13
 Run date 28FEB13
 Page number 4A
 © Primavera Systems, Inc.

Parsons Brinckerhoff Dudley Sq. Streetscape

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point
